

What happened? (activities made since the last follow up)

- * Interface Adjustments for Firefox
- * Adjustments in relation with the test's results (according to the testing plan #1)
- * Testing Plan #2 Elaboration
- * Execution of the second group of tests

What should have happened? (activities until the follow up date)


- * Ajax implementation for the wi3 login/logout module
- * General Agenda Implementation
- * Mailings culmination (interface considerations)

Areas of attention

- * Login/logout adjustments
- * **Final Approval of the Requirements Specifications (Reviewed Version 17-Nov-2006 send by email to Arne Postma)**

What are the next activities? (Tasks and responsibilities)

- * Login/logout adjustments. Person in charge: GWT 06 Dec 2006
- * Mailings culmination. Person in charge: GWT 06 Dec 2006
- * General Agenda Implementation. Person in charge: GWT 07 Dec 2006
- * Adjustments in relation with the test's results (according to the testing plan #2). Person in charge: GWT 8 Dec 2006
- * Final testing plan elaboration. Person in charge: GWT 10 Dec 2006
- * Tests execution. Person in charge: Tierra 10-12 Dec 2006
- * Execution of the programmed activities (According to the plan)
- * Next meeting 13 Dec 2006 (11 am Ccs)

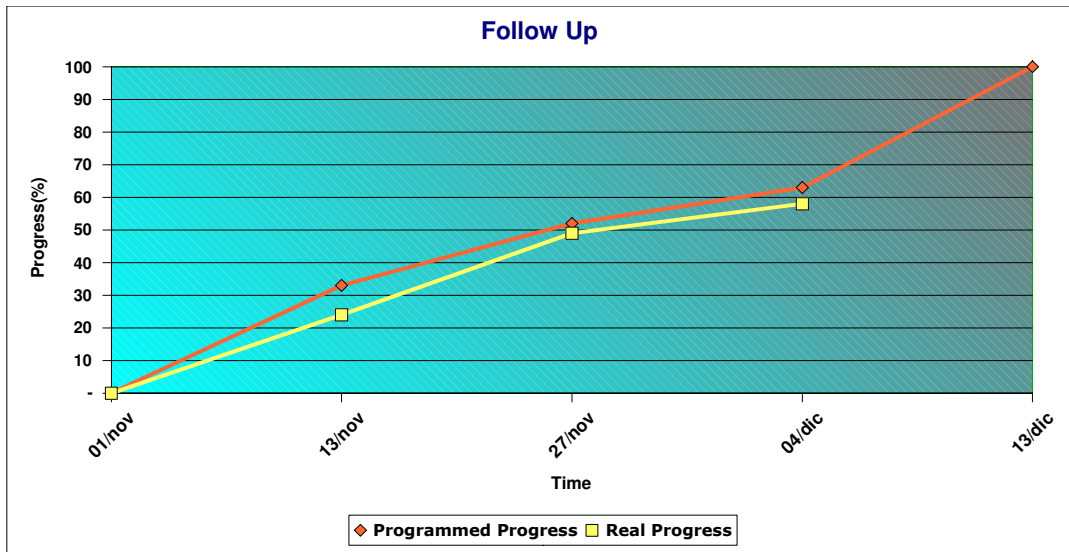

Date	1-nov	13-nov	27-nov	4-dic	13-dic
Programmed	0,00	33,00	52,00	63,00	100,00
Real	0,00	24,00	49,00	58,00	0,00

Legend	
●	Deviation <= 5%
●	Deviation > 5% y Deviation <= 10%
●	Deviation > 10%

Follow Up	Programmed Progress	Real Progress
01/nov	-	-
13/nov	33,00	24,00
27/nov	52,00	49,00
04/dic	63,00	58,00
13/dic	100,00	
